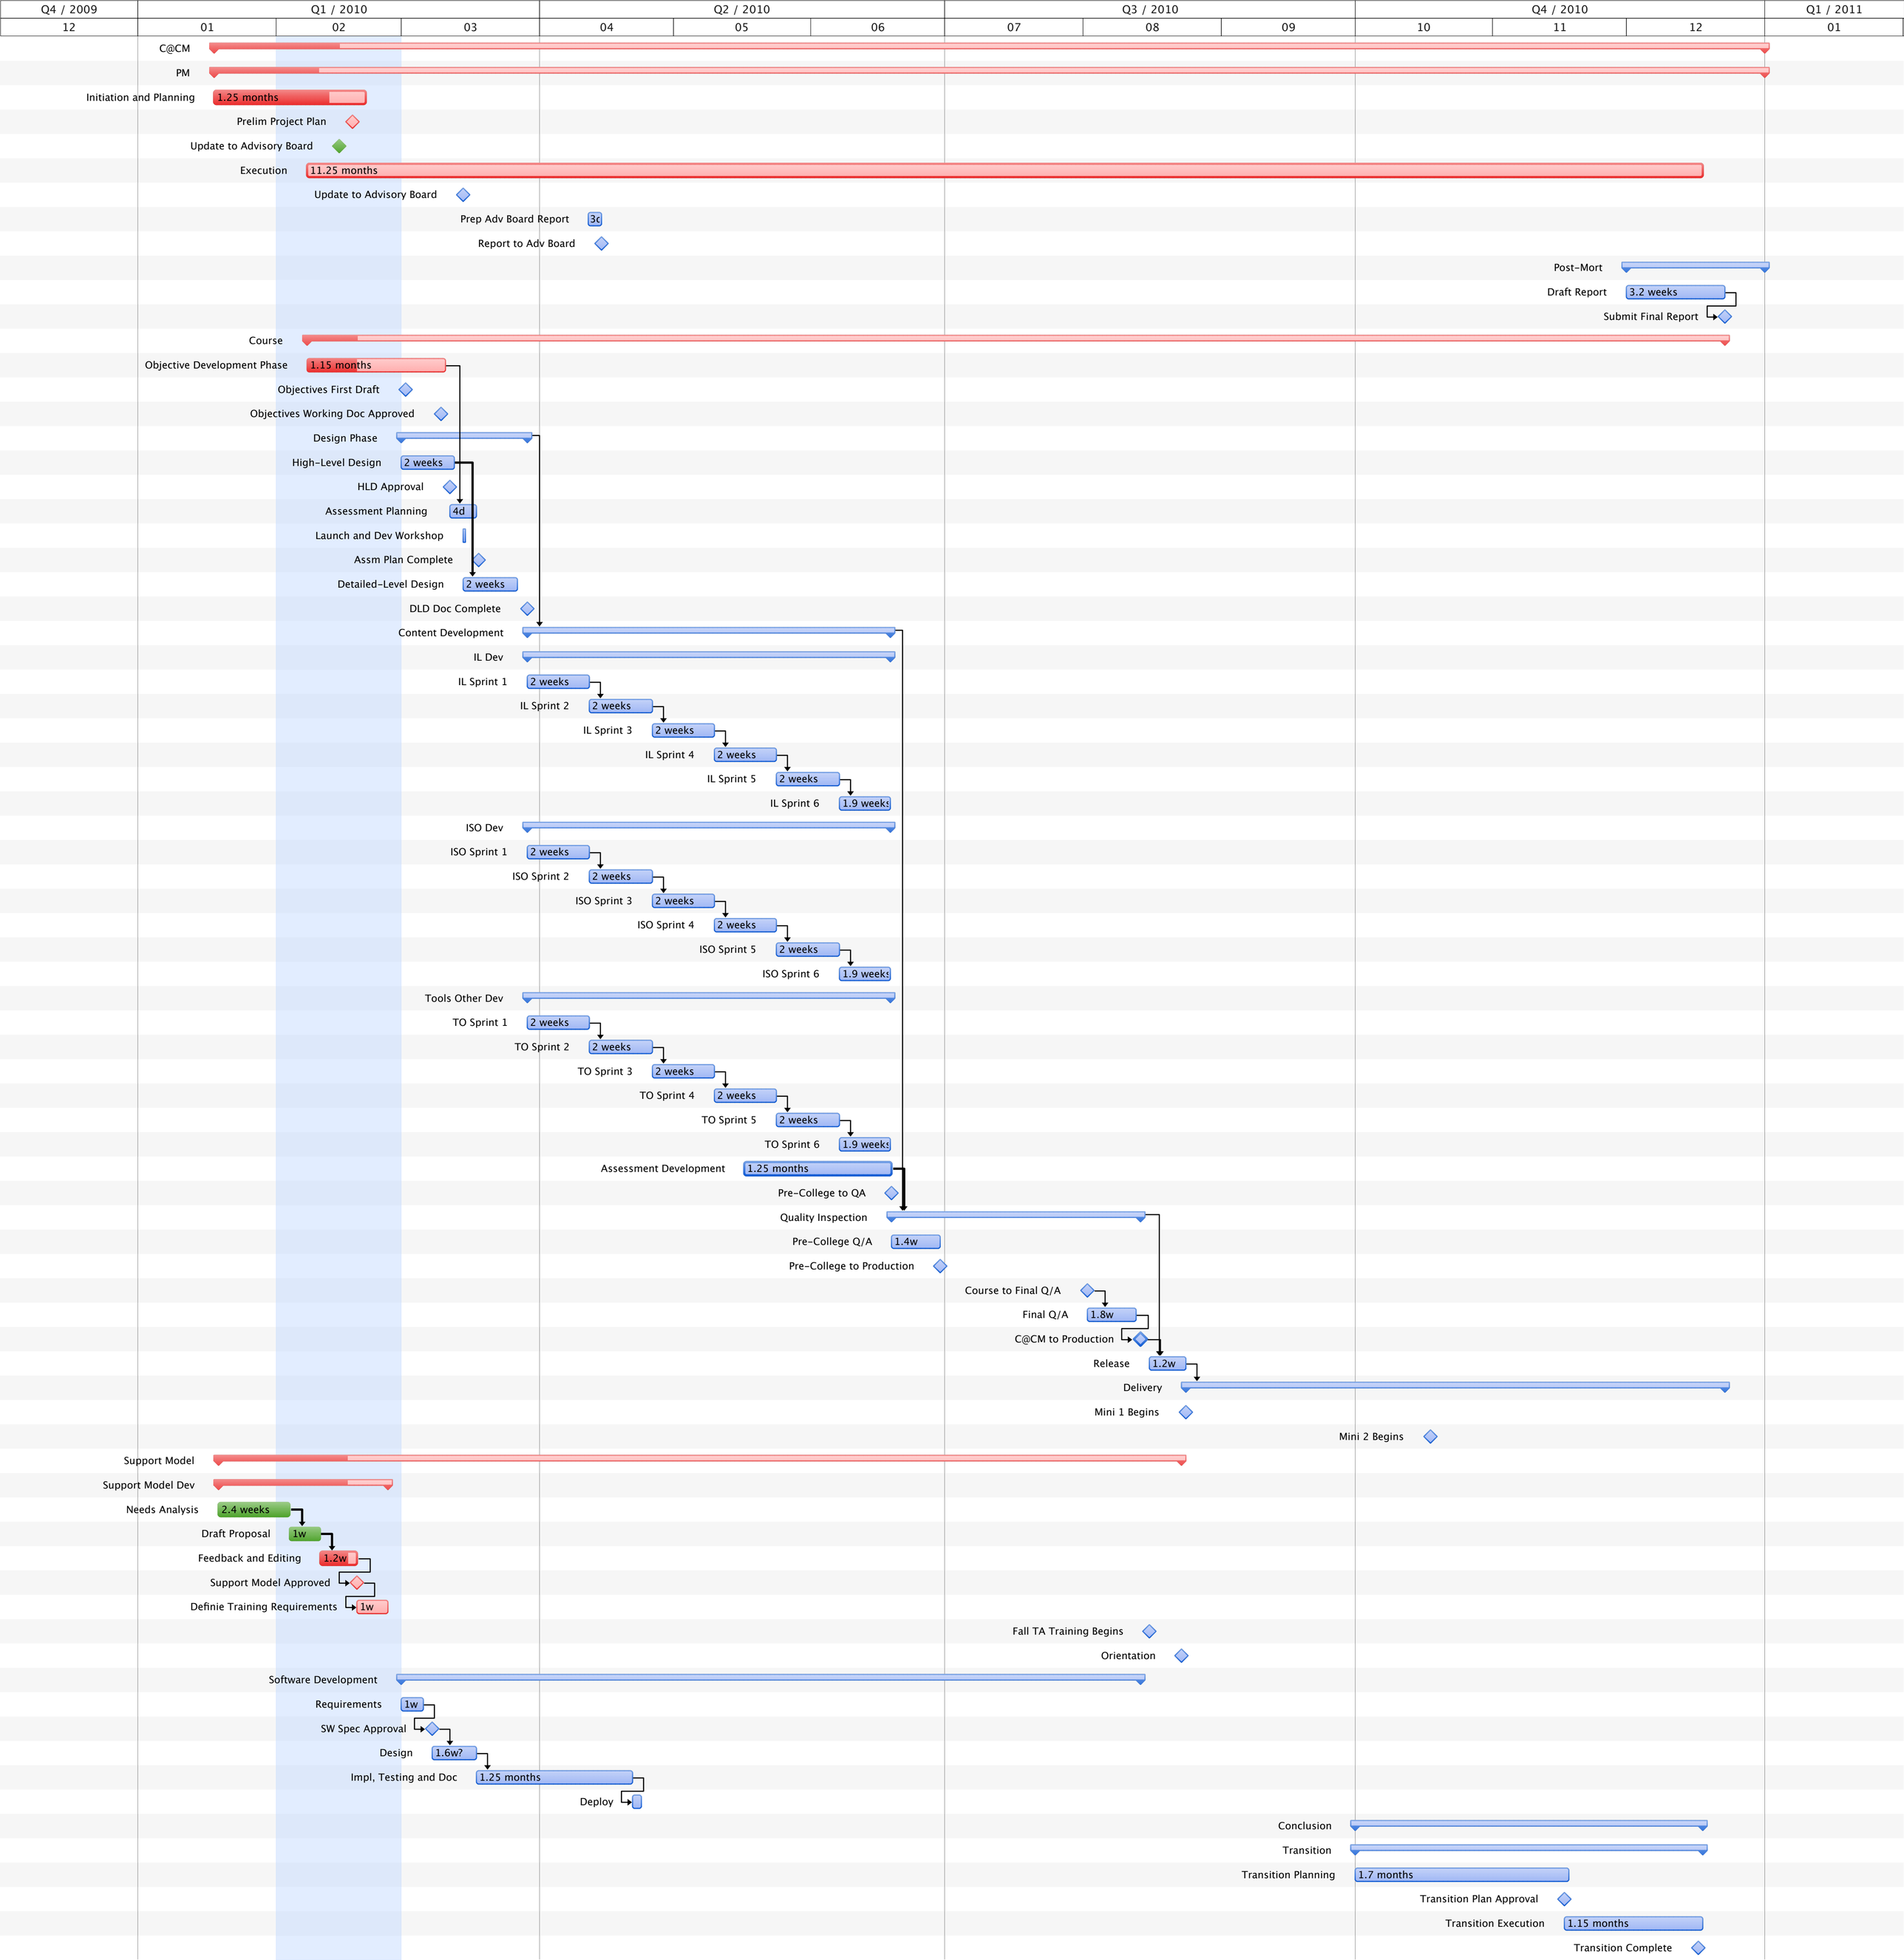
Q4 / 2009
Q1 / 2010
Q2 / 2010
Q3 / 2010
Q4 / 2010
Q1 / 2011
12
01
02
03
04
05
06
07
08
09
10
11
12
01
C@CM
PM
Initiation and Planning
1.25 months
Prelim Project Plan
Update to Advisory Board
Execution
11.25 months
Update to Advisory Board
Prep Adv Board Report
3c
Report to Adv Board
Post-Mort
Draft Report
3.2 weeks
Submit Final Report
Course
Objective Development Phase
1.15 months
Objectives First Draft
Objectives Working Doc Approved
Design Phase
High-Level Design
2 weeks
HLD Approval
Assessment Planning
4d
Launch and Dev Workshop
Assm Plan Complete
Detailed-Level Design
2 weeks
DLD Doc Complete
Content Development
IL Dev
IL Sprint 1
2 weeks
IL Sprint 2
2 weeks
IL Sprint 3
2 weeks
IL Sprint 4
2 weeks
IL Sprint 5
2 weeks
IL Sprint 6
1.9 weeks
ISO Dev
ISO Sprint 1
2 weeks
ISO Sprint 2
2 weeks
ISO Sprint 3
2 weeks
ISO Sprint 4
2 weeks
ISO Sprint 5
2 weeks
ISO Sprint 6
1.9 weeks
Tools Other Dev
TO Sprint 1
2 weeks
TO Sprint 2
2 weeks
TO Sprint 3
2 weeks
TO Sprint 4
2 weeks
TO Sprint 5
2 weeks
TO Sprint 6
1.9 weeks
Assessment Development
1.25 months
Pre-College to QA
Quality Inspection
Pre-College Q/A
1.4w
Pre-College to Production
Course to Final Q/A
Final Q/A
1.8w
C@CM to Production
Release
1.2w
Delivery
Mini 1 Begins
Mini 2 Begins
Support Model
Support Model Dev
Needs Analysis
2.4 weeks
Draft Proposal
1w
Feedback and Editing
1.2w
Support Model Approved
Definie Training Requirements
1w
Fall TA Training Begins
Orientation
Software Development
Requirements
1w
SW Spec Approval
Design
1.6w?
Impl, Testing and Doc
1.25 months
Deploy
Conclusion
Transition
Transition Planning
1.7 months
Transition Plan Approval
Transition Execution
1.15 months
Transition Complete
